



Network Statement 2022 – Appendix 3.5B




Appendix 3.5B

Contents	Page
1. Long-distance lines	
Overview of the Long-distance lines	3
TIB 1 – 35	5 - 8
2. S-Lines	
Overview of the S-Lines	4
TIB 810 – 880	9

Fjernbanen TIB 1, 2, 5, 21, 23, 26

Netredegørelsen 2022 - overblik 2023


- Sprogø - Korsør**
Tunnelarbejde
- Middelfart - Nyborg**
Middelfart – Nyborg
- (Næstved) – (Lundby)**
Tredjeparts-projekt
- (Vordingborg) - Orehoved**
Storstrømsbroen, Ringsted Femern
- Nykøbing F Vest**
Ringsted Femern
- (Nykøbing F. V) - Rødby Færge**
Ringsted Femern
- (Holbæk) – Kalundborg**
Roskilde - Kalundborg
- Odense – Fruens Bøge**
Forberedende arbejder EP Fredericia - Aarhus, broarbejder
- Fredericia – Vejle**
Ballastrensning
- Vejle – Horsens + Hørning – Aarhus**
Forberedende arbejder EP Fredericia - Aarhus, broarbejder
- Kolding - Vamdrup**
Fredericia – Padborg sporombygning

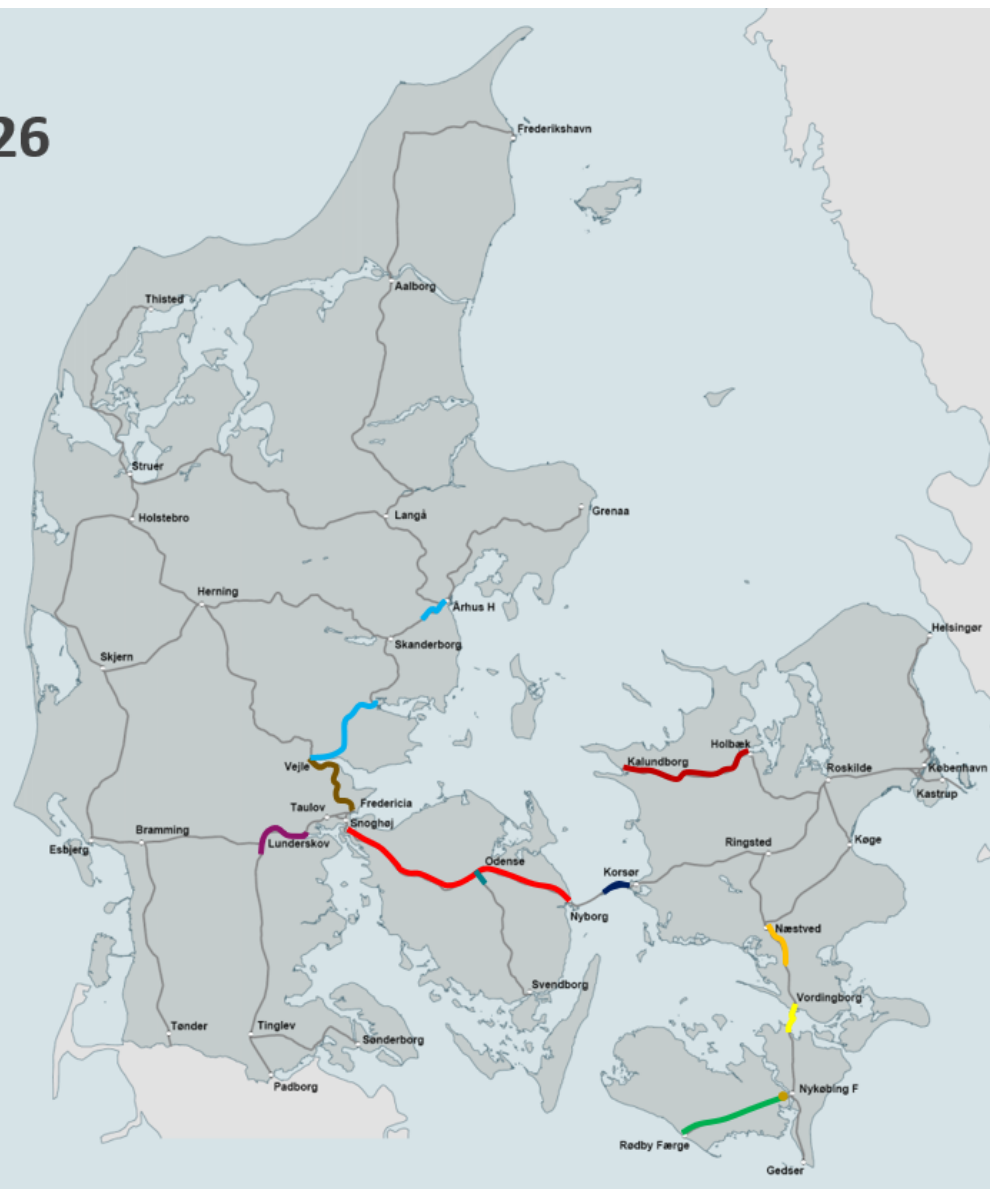

S-banen

Netredegørelsen 2022 - overblik 2023

- Jægersborg - Hillerød
Signalprogrammet
- Ny Ellebjerg - Hillerød
Signalprogrammet

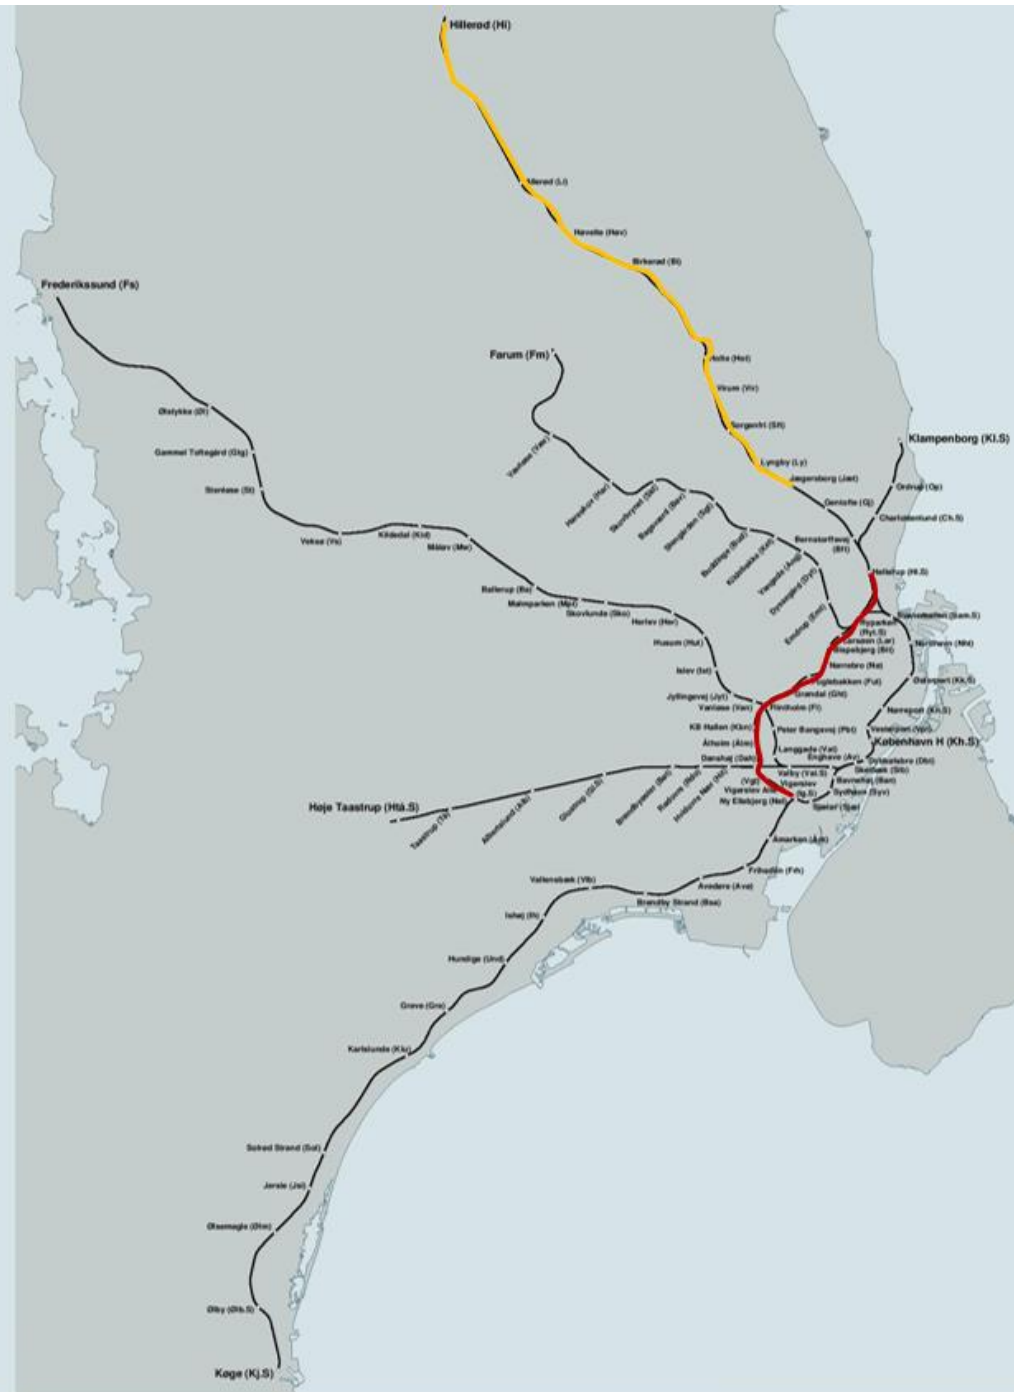

Serial no.	TIB	Line	Project	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation, cf. Annex VII
	1	Ringsted (Excl.) – Roskilde (Excl.)	Reconstruction of tracks	Track and bridge works		May-August	27/5 – 13/8	11 weeks single track possession One track possessed at a time on the line Ro-Rg.	Banedanmark	XXXX
	1	Korsør (incl.)	Speed upgrade	Exchange of 12 switches	5 days	July	22/07 – 31/07	Total closure of lines	Sund og Bælt	
	1	Sprogø (incl.) – Korsør (incl.)	Renovation of pump sump	Tunnel works	2 weeks	June	02/06 – 18/06	Possession of 2. main track Kø-Spr for constantly 15 days	Sund og Bælt	XXXX
	1	Sprogø (incl.) – Korsør (incl.)	Renovation of pump sum	Tunnel works	2 weeks	June - July	18/06 – 03/07	Possession of 1. main track Spr- Kø for constantly 15 days	Sund og Bælt	XXXX
2	1	Nyborg (excl.) – Ullerslev (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 132-141 (Nyborg - Ullerslev)	22 days	May – June	24/05 – 15-06	Left track operations Nyborg-Ullerslev	Banedanmark	High
3	1	Ullerslev (excl.) – Nyborg (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 132-141 (Nyborg - Ullerslev)	22 days	June – July	15/06 – 07-07	Left track operations Ullerslev-Nyborg	Banedanmark	High
4	1	Nyborg (excl.) – Odense (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Soft ground exchange Km 132-160 (Nyborg - Odense)	12 days	July	07/07 – 20/07	Total closure of lines	Banedanmark	High
5	1	Ullerslev (excl.) – Marslev (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 141-151 (Ullerslev - Marslev)	11 days	July	20/07 – 31/07	Left track operations Ullerslev-Marslev	Banedanmark	High
6	1	Marslev (excl.) – Ullerslev (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 141-151 (Ullerslev - Marslev)	25 days	July - August	31/07 – 25/08	Left track operations Marslev-Ullerslev	Banedanmark	High
7	1	Marslev (excl.) – Odense (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 151- 160 (Marslev - Odense)	5 days	August	25/08 – 30/08	Left track operations Marslev-Odense	Banedanmark	Medium
8	1	Odense (excl.) – Marslev (excl.)	NFSP0516 & NA0037 Middelfart -	Track works Km 151- 160 (Marslev - Odense)	27 days	August - September	30/08 – 26/09	Left track operations Odense-Marslev	Banedanmark	High

Serial no.	TIB	Line	Project	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation, cf. Annex VII
				Nyborg track renewal and speed upgrade						
9	1	Odense (incl.) – Odense (incl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Drainage works between track 2 & 3 Odense Station	Not clarified	Summer	Summer	Possession of tracks 2 & 3	Banedanmark	*
10	1	Odense (incl.) – Odense (incl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works in B track	50 days	Summer	Summer	Total closure of B track	Banedanmark	Major
11	1	Odense (incl.) – Holmstrup (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 161.4-162.4 & Km 168-170	11 days	September – October	26/09 – 07/10	Possession of track 5 Left track operations Odense-Holmstrup	Banedanmark	High
12	1	Holmstrup (excl.) – Odense (incl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 161.4-162.4	11 days	October	07/10 – 18/10	Possession of track 4 Left track operations Holmstrup-Odense	Banedanmark	High
13	1	Ejby (excl.) – Aarup (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 185-187	3 days	October	19/10 – 22/10	Left track operations Ejby-Aarup	Banedanmark	Medium
14	1	Kauslunde (excl.) – Middelfart (excl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works Km 205,3-209,5	3 days	October	22/10 – 25/10	Left track operations Kauslunde-Middelfart	Banedanmark	Medium
15	2	Næstved (excl.) – Lundby (excl.), Mogenstrup	RFB 3. party project (DSB)	Preparation and mounting of switches	3 weekends	March-June	Not settled	Total closure of both main tracks	Banedanmark	Medium
16	2	Lundby (excl.) – Næstved (excl.), Mogenstrup	RFB 3. party project (DSB)	Works regarding line lead, adjustment of tracks, etc.	2 weekends	March-June	Not settled	Right track	Banedanmark	Medium
17	2	Vordingborg (excl.) – Orehoved (excl.)	RFB	Establishment of <i>one other</i> track connection for the New Storstrøm Bridge	Time schedule not settled	March-April	March-April	Total closure of lines	Banedanmark	*
18	2	Vordingborg (excl.) – Orehoved (excl.)	RFB	Establishment of the <i>other</i> track connection for the New Storstrøm Bridge	Time schedule not settled	September –October	Not settled	Total closure of lines	Banedanmark	*
19	2	Nykøbing F Vest (incl.)	RFB	Placing of rolling stock, etc. Shunting to	All year round	All year round	Not settled	Track 1 (I signal D to U signal B)	Banedanmark	Major

Serial no.	TIB	Line	Project	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation, cf. Annex VII
				and from the work track				Lokaltog can operate to Nykøbing F St.		
								LA40 at Frederik IX's Bridge. 1,2 km, duration: the entire year		
20	2	Nykøbing F Vest (incl.)	RFB	Mounting of new switches		-	Not settled	Total closure of lines	Banedanmark	*
21	2	Nykøbing F Vest (excl.) – Rødby Færge (incl.)	RFB	Soft ground works, preparations for double track			Not settled	Total closure of lines	Banedanmark	Major
22	5	Holbæk (excl.) - Kalundborg (incl.)	Roskilde - Kalundborg	1 year adjustment	14 x 9 hours	July	14/7-28/7	No trains	Banedanmark	High
	11	Kalvebod (ekskl) – Vigerslev. (incl.)	METRO	Gangway tunnel, tracks 21 + 22 possessed in Vigerslev TIB 6 not affected.	2023-2024	07-09.04 05-07.05 27-29.05		Total closure of lines on IB 11		
23	21	Odense (incl.) – Fruens Bøge (incl.)	NFSP0516 & NA0037 Middelfart - Nyborg track renewal and speed upgrade	Track works km 161.4-162.4	11 days	26-06 (evening)	07-07 (evening)	Total closure of lines Odense-Fruens Bøge	Banedanmark	High
	23	Fredericia (Incl.) - Fredericia (Incl.)	Fredericia station	Removal of DV-signal, new tracks in total, exchange of switch, etc.	3 weeks	2. + 3. quarter	13/5 – 15/8	Is under cover of the works between Fa-Bk Ballast cleaning	Bdk	XXXX
24	23	Fredericia (incl.) – Vejle (incl.)	Ballast cleaning Fredericia - Vejle	Ballast cleaning + track renewal	90 days	2. + 3. quarter	13/5 – 15/8	Single track operation either Fredericia – Børkop / Børkop – Fredericia / Børkop – Vejle / Vejle - Børkop	Banedanmark	Major
25	23	Vejle (incl.) – Hedensted (incl.)	Preparatory works FA-AR	New bridge, same place Bridge 20596	1 x weekend possession	February	24/2-26/2	Total closure of lines	Banedanmark	Medium
26	23	Vejle (incl.) – Hedensted (incl.)	Preparatory works FA-AR	New bridge, same place Bridge 20596	4 x day possession	March	3/3-6/3	Total closure of lines	Banedanmark	Medium
	23	Vejle (excl.) – Hedensted (excl.)		Reisolation of bridges	6 weeks + 1 weekend	3. quarter	07/7-21/8	All trains through left track either Vj-Hed or Hed-Vj	BDK	XXXX
27	23	Vejle (incl.) – Hedensted (incl.)	Preparatory works FA-AR	New bridge, same place Bridge 20596	1 x weekend possession	October	20/10-22/10	Total closure of lines	Banedanmark	Medium
28	23	Vejle (incl.) – Hedensted (incl.)	Preparatory works FA-AR	New bridge, same place	4 x day possession	October	28/10-31/10	Total closure of lines	Banedanmark	Medium

Serial no.	TIB	Line	Project	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation, cf. Annex VII
29	23	Hedensted (incl.) – Horsens (incl.)	Preparatory works FA-AR	Bridge 20596 Bridge lifting Bridge 20660	1 x weekend possession	February	23/2-25/2	Total closure of both tracks Hedensted – Horsens	Banedanmark	Medium
30	23	Hedensted (incl.) – Horsens (incl.)	Preparatory works FA-AR	Bridge lifting Bridge 20660	4 x day possession	March	3/3-6/3	Total closure of both tracks Hedensted – Horsens	Banedanmark	Medium
31	23	Hedensted (incl.) – Horsens (incl.)	Preparatory works FA-AR	Bridge lifting Bridge 20660	10 x day possession	March	7/3-16/3	Left track operations Horsens - Hedensted	Banedanmark	High
32	23	Hedensted (incl.) – Horsens (incl.)	Preparatory works FA-AR	Bridge lifting Bridge 20660	2 x day possession	March	17/3-18/3	Left track operations Hedensted – Horsens	Banedanmark	Medium
33	23	Hedensted (incl.) – Horsens (incl.)	Preparatory works FA-AR	Bridge lifting Bro 20660	1 x weekend possession	May	5/5-7/5	Total closure of both tracks Hedensted – Horsens	Banedanmark	Medium
34	23	Hørning (incl.) – Aarhus (incl.)	Preparatory works Fa-Ar	Bridge lifting Bridge 20846	1 x day possession	June	24/6	Left track operations Hørning – Aarhus	Banedanmark	Medium
35	23	Hørning (incl.) – Aarhus (incl.)	Preparatory works Fa-Ar	Bridge lifting Bridge 20846	1 x weekend possession	July	28/7-30/7	Left track operations Hørning – Aarhus	Banedanmark	Medium
36	23	Hørning (incl.) – Aarhus (incl.)	Preparatory works Fa-Ar	Bridge lifting Bridge 20848	3 months day possession	June-August	1/6-31/8	Left track operations Aarhus – Hørning	Banedanmark	Major
37	23	Hørning (incl.) – Aarhus (incl.)	Preparatory works Fa-Ar	Bridge lifting Bridge 20848	2 x weeks possession	June-August	11/6-13/6 30/7-1/8	Total closure of lines Hørning – Aarhus	Banedanmark	High
38	23	Hørning (incl.) – Aarhus (incl.)	Preparatory works Fa-Ar	Bridge lifting Bridge 20848	8 x day possession	December	8/12-16/12	Left track operations Hørning – Aarhus	Banedanmark	High
39	23	Hørning (incl.) – Aarhus (incl.)	Preparatory works FA-AR	Exchange of bridge deck Bridge 20852	3 months day possession	June-August	1/6– 31/8	Left track operations Aarhus – Hørning	Banedanmark	Major
40	23	Hørning (incl.) – Aarhus (incl.)	Preparatory works FA-AR	Sidewise removal of track Bridge 20876	21 day possessions	3. quarter	Not settled	Aarhus: AI traffic to/from south through tracks 30, 40 and 80.	Banedanmark	High
41	23	Hørning (incl.) – Aarhus (incl.)	Preparatory works FA-AR	Sidewise removal of track Bridge 20876	21 day possessions	3. quarter	Not settled	Aarhus: AI railway traffic to/from south through tracks 30, 50 and 80 LA40 in track 50	Banedanmark	High
42	26	Kolding (incl.) – Lunderskov (Incl.)	Reconstruction of tracks	Ballast cleaning + track renewal	17 days	July	14/7 – 30/7	Left track operations	Banedanmark	High

Serial no.	TIB	Line	Project	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation, cf. Annex VII	
43	26	Lunderskov (incl.) – Vamdrup (incl.)	Fredericia - Padborg	Reconstruction of tracks	Ballast cleaning + track renewal	10 days	July-August	30/7 – 8/8	Koldning - Lunderskov	Banedanmark	High
44	26		Fredericia - Padborg	Reconstruction of tracks	Ballast cleaning + track renewal	8 days	August	8/8 – 15/8	Left track operations Lunderskov - Vamdrup	Banedanmark	High

Serial no.	TIB	Line	Project	Description	Exp. duration	Exp. period	Exp. dates	Traffic impact	Builder	Categorisation, cf. Annex VII
1	820 880	Jægersborg (incl.) - Hillerød (incl.) Ny Ellebjerg (incl.) - Hellerup (incl.)	New signalling system,S-Line PSP: S/SB/BBFB-9-9-11160-SHBD	Putting into service of "postponed deliveries"	1 weekend	March	25/3-27/3	Total closure of lines	Banedanmark	
